


Britannia Heritage Shipyard Society

Work Plan

Iona Maintenance

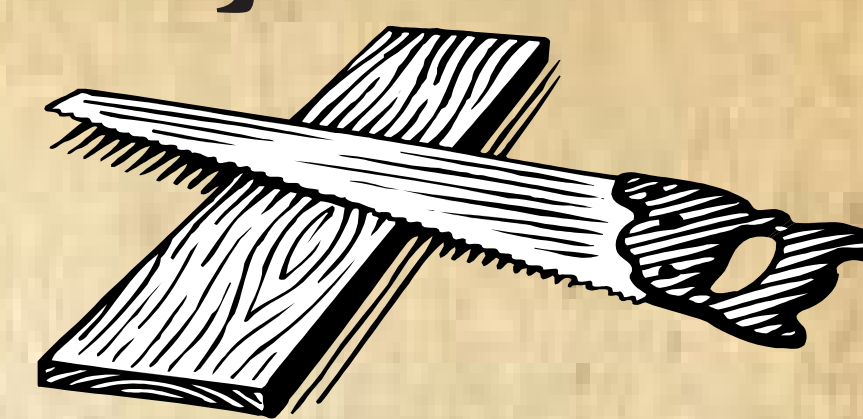

Area	Steps	Shifts (4 hrs)
Hull - exterior	- Remove coolant, exit tubes	1
	- Reef plank seams not previously done this year below water line	6
	- Caulk, paint, pay seams	3
Hull - interior	- Apply backing blocks on seams, where necessary	3
	- Rebuild drive shaft cover boards	2
	- Install fish hold floor boards (x2)	4
Engine	- Change transmission oil	1
Fuel Tanks	- Flush	1
	- Connect fuel line	1
Transom	- Rebuild transom frame (esp. below water line)	20
	- Rebuild rub strakes	6
Cabin - exterior	- Remove/replace fiberglass/epoxy on trunk cabin top with canvas	4
	- Replace starboard trunk cabin hand rail with oak	2
Cabin - interior	-	
Wiring/Electrical	- Supply shore power cable	1
	- Install new voltage regulator	2
	- Remove existing wiring	1
	- Build battery hold down system	2
	- Build battery box lid	3
	- Install new wiring incl. breakers, nav lights, interior cabin lights, pumps, etc.	10
Hardware & Fittings	- Mooring line cleats (port & starboard)	2
	- Bumber rings	2
Ballast	- Additional weight to hull, esp. stern	2
Total	4 hour shifts	79

Relaunch in April 2010
